

JONESBORO ANIMAL SHELTER

PROGRESS REPORT

7/3/2007

All subcontracts have been written and materials have been ordered. Shop drawings from all subcontractors are being drawn and forwarded to the architect for approval. Shop drawings are the documents drawn up by each subcontractor or material supplier that details each item they provide more thoroughly than what would be practical to put on the Construction Drawings.

Shop drawings are being delivered to Nabholz from the subcontractor/material supplier. We are forwarding the shop drawings on to the architect who will make changes, approve, or reject them. They'll come back to Nabholz and will be forwarded back to the sub/supplier, which will allow them to begin fabrication.

The primary focus is being put on the concrete reinforcing and pre-engineered metal building shop drawings. The reinforcing shop drawings are needed quickly because this steel will be one of the first things we need on the project. The pre-engineered metal building shop drawings usually take the longest time to receive, and the fabrication of the building can take up to three months once they've been approved.

The building permit process is almost complete, and the City should be starting dirt work very soon. When the road is extended, and the building pad constructed, we will then begin digging footings, and setting up the concrete slab.

JONESBORO ANIMAL SHELTER
6119 Highland Ave.

PROGRESS REPORT

8/7/2007

The site has been moved from the west side of the extended road, to the east side, and it has also been moved north. Associated Engineering is currently producing revised site drawing reflecting these changes. These changes were requested by the City to aid in site drainage. The City has given us a "grading only" permit, and the permanent building permit will be issued when these revisions are drawn and submitted.

The dirtwork required to extend the road and construct the building pad has been started by the City. This work will continue on through this week. Building reinforcing steel is to be delivered on Monday of next week. Once the building pad is finished, we will begin digging footings and installing rebar.

Kennel shopdrawings have been received at the Nabholz office, and will be forwarded to the architect after our review and mark-up. The pre-engineered metal building has been ordered and is scheduled to ship around the second week of October, which fits in with our overall schedule.

**JONESBORO ANIMAL SHELTER
PROJECT SCHEDULE**

Act ID Description Dur Start Finish MAY JUN JUL AUG SEP OCT NOV DEC JAN FEB MAR
21 28 04 11 18 25 02 09 16 23 30 06 13 20 27 03 10 17 24 01 08 15 22 29 05 12 19 26 03 10 17 24 31 07 14 21 28 04 11 18 25 03 10 1

ADMINISTRATIVE PHASE

02690	Construction Management Contract Signed	0	24MAY07 A	13JUL07 A	▼ Construction Management Contract Signed
02700	Building Permit Process	10	24MAY07 A	13JUL07 A	▼ Building Permit Process
02710	Initiate Submittals	20	11JUN07 A	17AUG07	▼ Initiate Submittals
02740	Initiate Rebar Submittals	10	11JUN07 A	13JUL07 A	▼ Initiate Rebar Submittals
02730	Preconstruction Meeting	1	20JUN07 A	20JUN07 A	▼ Preconstruction Meeting
02720	GC/Arch. Approve Submittals	30	15JUL07 A	17AUG07	▼ GC/Arch. Approve Submittals
02750	GC/Arch. Approve Rebar Submittals	1	16JUL07 A	16JUL07 A	▼ GC/Arch. Approve Rebar Submittals

FABRICATION / DELIVERY

03130	Fabricate Reinforcing Steel	10	17JUL07 A	30JUL07 A	▼ Fabricate Reinforcing Steel
03120	Fabricate Pre Engineered Metal Building	60	23JUL07 A	19OCT07	▼ Fabricate Pre Engineered Metal Building
03360	Fabricate Hourquaters Kennels	60	20AUG07	09NOV07	▼ Fabricate Hourquaters Kennels

PRODUCTION

03160	Earthwork - Road Construction	30	11JUL07 A	24AUG07	▼ Earthwork - Road Construction
03170	Dig & Pour Footings Complete	5	27AUG07	31AUG07	▼ Dig & Pour Footings Complete
03180	Set Forms - Pour Office Slab	5	03SEP07	07SEP07	▼ Set Forms - Pour Office Slab
03220	Rough-in Under slab MEP	10	03SEP07	14SEP07	▼ Rough-in Under slab MEP
03190	Set Forms and Pour Kennel Area	10	10SEP07	21SEP07	▼ Set Forms and Pour Kennel Area
03200	Erect Primary Framing	5	18OCT07	22OCT07	▼ Erect Primary Framing
03210	Erect Secondary Framing	5	23OCT07	29OCT07	▼ Erect Secondary Framing
03300	Install Metal Roof	10	30OCT07	12NOV07	▼ Install Metal Roof
03230	Metal Studs and Exterior Sheathing	30	08NOV07	17DEC07	▼ Metal Studs and Exterior Sheathing
03250	Masonry Complete	10	06NOV07	19NOV07	▼ Masonry Complete
03240	Rough-in MEP	20	13NOV07	10DEC07	▼ Rough-in MEP
03280	Window & Exterior Door Installation	5	20NOV07	28NOV07	▼ Window & Exterior Door Installation
03370	Install Kennels and Guillotine Doors/Walls	20	20NOV07	17DEC07	▼ Install Kennels and Guillotine Doors/Walls
03270	Exterior Sheeting and Soft	15	27NOV07	17DEC07	▼ Exterior Sheeting and Soft
03290	Install Drywall	25	27NOV07	02JAN08	▼ Install Drywall
03280	Tape - Bed - Paint Interior Walls	20	11DEC07	09JAN08	▼ Tape - Bed - Paint Interior Walls
03350	HVAC System Testing - Adjusting - Balancing	15	11DEC07	02JAN08	▼ HVAC System Testing - Adjusting - Balancing
03300	Install Ceiling Grid	4	14DEC07	19DEC07	▼ Install Ceiling Grid
03330	Install Ceiling Tile	2	20DEC07	21DEC07	▼ Install Ceiling Tile
03310	Set Millwork	15	03JAN08	23JAN08	▼ Set Millwork
03320	Install Flooring	15	17JAN08	08FEB08	▼ Install Flooring
03340	Final Paint & Clean	5	07FEB08	13FEB08	▼ Final Paint & Clean

CLOSEOUT PHASE

03060	Closeout Planning Meeting	1	26DEC07	26DEC07	▼ Closeout Planning Meeting
03090	Create Worklists - Correct Deficiencies	35	27DEC07	14FEB08	▼ Create Worklists - Correct De
03100	Collect Closeout Documents	35	27DEC07	14FEB08	▼ Collect Closeout Documents
03110	City of Jonesboro - Final Inspection	1	14FEB08	14FEB08	▼ City of Jonesboro - Final Insp
03140	Certificate of Occupancy Received	1	15FEB08	15FEB08	▼ Certificate of Occupancy Rec
03150	Final Inspection and Walkthrough	1	18FEB08	18FEB08	▼ Final Inspection and Walk
03070	Substantial Completion	0		18FEB08	▼ Substantial Completion

JONESBORO FIRE STATION #3

PROGRESS REPORT

7/3/2007

All subcontracts have been written and materials have been ordered. Shopdrawings from all subcontractors are being drawn and forwarded to the architect for approval.

Nabholz received revised site drawings on 6/26, and construction has progressed to the detention pond, and added parking. The building pad is almost complete. Once the existing power pole has been removed from the building pad, we will begin digging footings and pouring concrete. AT&T and Suddenlink both have the removal of their lines scheduled, and have told me that they will do everything in their power to remove them as quickly as possible. City Water and Light has already removed and relocated their power lines from this pole.

We will be receiving reinforcing steel for the building on Thursday, 7/5, and look forward to beginning foundation work as soon as the power pole is removed.

JONESBORO FIRE STATION #3
2212 Brazos

PROGRESS REPORT

8/7/2007

Footing and foundation work is currently being performed, and underslab plumbing rough-in is being completed. We plan on pouring our first section of slab on Friday, August, 10. Further slab pours will be set up and poured through the end of this month and into September. The training room and bunk areas will be poured first, with the apparatus bay being the last area poured.

Structural steel is set to arrive on the project at the end of August. Bar joists and metal decking will arrive the first week of September. After the slabs are poured, we will let the concrete cure until it achieves design strength, then begin load bearing masonry construction and steel erection.

Metal framing, sheathing, blocking, and roofing will follow up behind the steel erectors. This will put the building "in the dry" by the middle of December.

JONESBORO FIRE STATION #7
8461 CW Post Road

PROGRESS REPORT

7/3/2007

All subcontracts have been written and materials have been ordered. Shop drawings from all subcontractors are being drawn and forwarded to the architect for approval.

Revised site plans were issued on 6/26 and Nabholz received the building permit for the project on 7/2. Storm drainage work, erosion control, and site work will begin immediately.

JONESBORO FIRE STATION #7
8461 CW Post Road

PROGRESS REPORT

8/7/2007

The building pad dirtwork will be 100% complete this week. Reinforcing steel for the project has been delivered and footing installation will begin next week. Under-slab plumbing rough-in will start shortly after the footing work is started. We will set up this slab to be poured in the same manner as JFD #3, with the bunks and living areas coming first, and the apparatus bay being poured last.

The structural steel shopdrawings have been reviewed, marked up, and sent back to the steel fabricator. Conway Steel is the low bidder on both projects, and they will fabricate this steel after they are complete with JFD #3. Lacy's Welding will be performing the steel erection on both projects also, and this should work right in with our schedule.

Metal framing, sheathing, blocking, and roofing will follow up behind the steel erectors. This will put the building "in the dry" by the end of December.

Jonesboro Fire Department Phase 1
PROJECT SCHEDULE

Act ID	Description	Dur	Start	Finish	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR
--------	-------------	-----	-------	--------	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----


Act ID	Description	Dur	Start	Finish
02710	Schematic Design	4	16NOV06 A	21NOV06 A
02790	Schematic Drawing Review Meeting	1	21NOV06 A	21NOV06 A
02700	Design Development	10	22NOV06 A	05DEC06 A
02770	50% CD Review Meeting	1	06DEC06 A	06DEC06 A
02780	Construction Document Revisions	10	07DEC06 A	01FEB07 A
02800	90% CD Review Meeting	1	02FEB07 A	02FEB07 A
02810	Construction Document Revisions	10	05FEB07 A	30MAR07 A
02820	100% Construction Documents Issued	0	02APR07 A	
02830	Receive Sub-Bids	15	03APR07 A	26APR07 A
02840	City and State Plan Review	10	03APR07 A	02JUL07 A
02850	Establish GMP	2	22MAY07 A	23MAY07 A

Act ID	Description	Dur	Start	Finish
03080	Submit and Fabricate Building Steel	80	04JUN07 A	24SEP07
03100	Submit and Fabricate Rebar	20	04JUN07 A	31JUL07 A

Act ID	Description	Dur	Start	Finish
03260	Project Layout	2	04JUN07 A	05JUN07 A
03270	Earthwork - Cut and Fill	20	06JUN07 A	10JUL07 A
03250	Preconstruction Meeting	1	08JUN07 A	08JUN07 A
03280	Dig and Pour Footings	15	12JUL07 A	09AUG07
03290	Form Concrete Slab	15	10AUG07	30AUG07
03300	Install Below-slab Utilities	10	17AUG07	30AUG07
03310	Backfill - Compact - Fine Grade	10	31AUG07	13SEP07
03320	Pour Floor Slab	10	14SEP07	27SEP07
03330	Erect Steel	20	28SEP07	25OCT07
03350	Exterior Wall Framing - Masonry	20	26OCT07	22NOV07
03470	Metal Roofing Complete	10	26OCT07	08NOV07
03490	Install Interior Masonry Walls	15	26OCT07	15NOV07
03460	Interior Wall Framing	20	09NOV07	06DEC07
03340	Flat Roofing Complete	20	16NOV07	13DEC07
03370	Install Windows and Exterior Doors	10	16NOV07	29NOV07
03360	Rough-in MEP	20	23NOV07	20DEC07
03480	Hang Drywall	20	30NOV07	28DEC07
03380	Tape - Bed - Blockfill - Paint	25	14DEC07	21JAN08
03390	Install Ceiling Grid	20	08JAN08	04FEB08
03400	Set Millwork	10	22JAN08	04FEB08
03410	Trim-out MEP	15	22JAN08	11FEB08
03420	Hang Doors - Install Finish Hardware	10	22JAN08	04FEB08
03430	Flooring	20	29JAN08	25FEB08
03440	Install Acoustical Ceiling Tile	10	12FEB08	25FEB08
03450	Final Paint & Clean	5	26FEB08	03MAR08

Act ID	Description	Dur	Start	Finish
03090	Nabholz Pre-Final Inspection	1	22JAN08	22JAN08
03110	Pre-Punchlist Completion	23	23JAN08	22FEB08
03040	City of Jonesboro - Final Inspection	1	04MAR08	04MAR08

CLOSEOUT PHASE - BUILDING #3

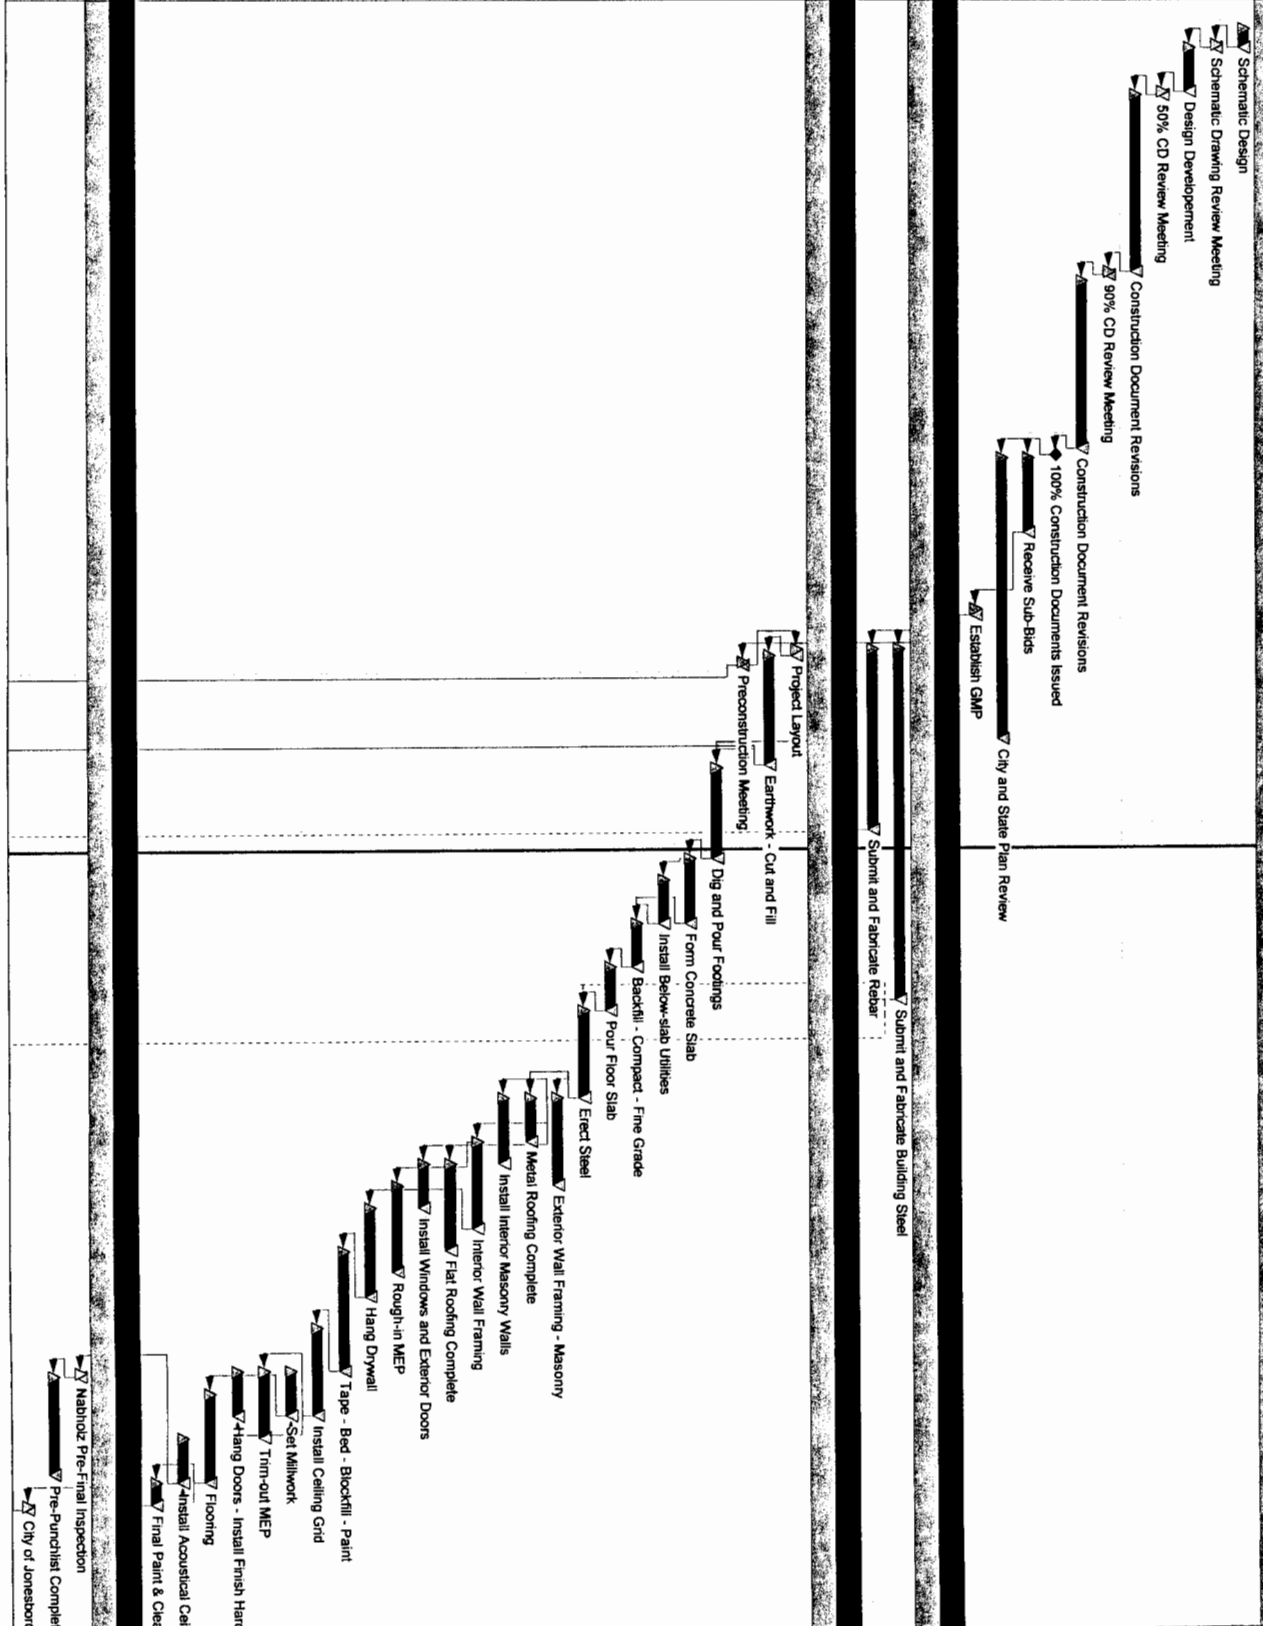


Act ID	Description	Dur	Start	Finish
03050	Certificate of Occupancy Received	1	05MAR08	05MAR08
03060	Final Building Inspection & Walk Through	1	06MAR08	06MAR08
03070	Substantial Completion - Building #3	0	06MAR08	06MAR08

PRODUCTION - BUILDING #7

0703250	Preconstruction Meeting	1	19JUN07	19JUN07
0703260	Project Layout	2	29JUN07	02JUL07
0703270	Earthwork - Cut and Fill	20	11JUL07	09AUG07
0703280	Dig and Pour Footings	13	10AUG07	28AUG07
0703290	Form Concrete Slab	17	29AUG07	20SEP07
0703300	Install Below-slab Utilities	10	05SEP07	18SEP07
0703310	Backfill - Compact - Fine Grade	11	21SEP07	05OCT07
0703320	Pour Floor Slab	6	08OCT07	15OCT07
0703330	Erect Steel	20	16OCT07	12NOV07
0703350	Exterior Wall Framing - Masonry	20	13NOV07	10DEC07
0703470	Metal Roofing Complete	10	13NOV07	26NOV07
0703490	Install Interior Masonry Walls	15	13NOV07	03DEC07
0703460	Interior Wall Framing	20	27NOV07	24DEC07
0703340	Flat Roofing Complete	15	04DEC07	24DEC07
0703370	Install Windows and Exterior Doors	15	04DEC07	24DEC07
0703360	Rough-in MEP	25	11DEC07	16JAN08
0703480	Hang Drywall	20	11DEC07	09JAN08
0703380	Tape - Bed - Blockfill - Paint	27	26DEC07	01FEB08
0703390	Install Ceiling Grd	15	21JAN08	08FEB08
0703400	Set Millwork	10	28JAN08	08FEB08
0703410	Trim-out MEP	17	28JAN08	19FEB08
0703420	Hang Doors - Install Finish Hardware	10	28JAN08	08FEB08
0703430	Flooring	20	11FEB08	07MAR08
0703440	Install Acoustical Ceiling Tile	7	11FEB08	19FEB08
0703450	Final Paint & Clean	5	06MAR08	12MAR08

CLOSEOUT PHASE - BUILDING #7

0703090	Nabholz Pre-Final Inspection	1	07FEB08	07FEB08
0703110	Pre-Punchlist Completion	23	08FEB08	11MAR08
0703040	City of Jonesboro - Final Inspection	1	13MAR08	13MAR08
0703050	Certificate of Occupancy Received	1	14MAR08	14MAR08
0703060	Final Building Inspection & Walk Through	1	17MAR08	17MAR08
0703070	Substantial Completion - Building #7	0	17MAR08	17MAR08

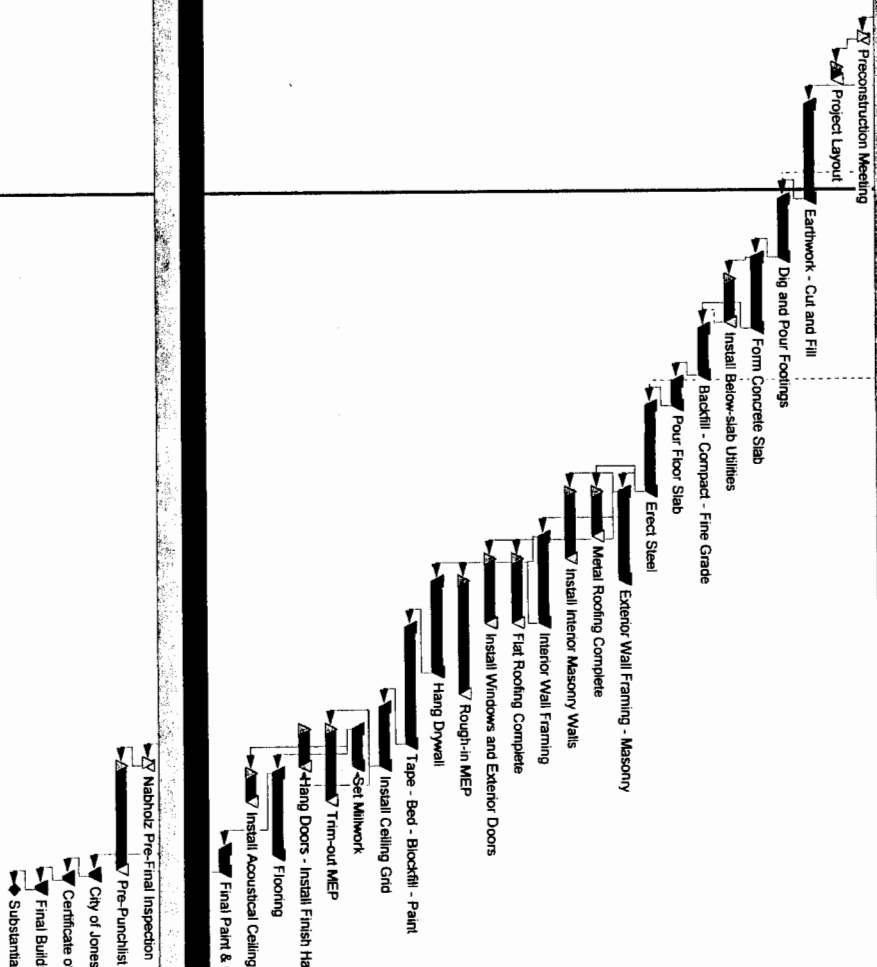

Summary Bar	Legend
Empty Start Point	Start Point
Empty End Point	End Point
Empty Bar	Activity
Partial Bar	Activity (Partial)
Full Bar	Activity (Complete)
Checkmark	Completed
Triangle	Start Point
Square	End Point

THIS SCHEDULE REMAINS THE PROPERTY OF NABHOLZ CONSTRUCTION CORPORATION
 IT IS PROVIDED FOR FACILITATING INFORMATION TO CONSTRUCT THE PROJECT
 LISTED AND DOES NOT CHANGE THE CONTRACTED COMPLETION DATE
